

جواب

سوال

<p>جی ہاں یہ درست ہے کہ چشمہ رائٹ بینک لفٹ کینال منصوبے سے ضلع ڈیرہ اسماعیل خان میں زرعی انقلاب آئے گا۔ کیونکہ اس منصوبے کی تکمیل پر ضلع ڈیرہ اسماعیل خان کی 1295000 ایکڑ اراضی زیر کاشت آجائے گی۔ اور پورا صوبہ زرعی لحاظ سے خود کفیل ہو جائے گا انشاء اللہ۔</p>	<p>(ا) کیا وزیر آبپاشی ازراہ کرم ارشاد فرمائیں گے کہ۔ (ا) آیا یہ درست ہے کہ صوبہ خیبر پختونخواہ چشمہ رائٹ بینک لفٹ کینال منصوبے سے زرعی لحاظ سے خود کفیل ہو سکتا ہے؟</p>
<p>چشمہ رائٹ بینک لفٹ کینال منصوبے کی تکمیل سے صوبے کو معاشی لحاظ سے استحکام میسر ہوگا۔ زرعی اجناس مثلاً گنا، گندم، چاول، مکئی، چھندر، کپاس، چنا، سورج کھسی، باجرہ اور سوسوں وغیرہ کی فصلات کی بکثرت پیداوار سے کسان خوشحال ہوگا۔ جو صوبے کی معاشی حالت بہتر بنانے میں کلیدی کردار ادا کرے گا۔ علاوہ ازیں لائیو سٹاک کی افزائش بہتر طریقے سے ہوگی جس سے دودھ کی پیداوار میں بھی اضافہ ہوگا۔</p>	<p>(ب) آیا یہ درست ہے کہ صوبے کی معیشت کے لیے نہایت اہم منصوبہ ہے؟</p>
<p>جی ہاں سابقہ وزرائے اعلیٰ خیبر پختونخواہ نے اس اہم منصوبے کو حتمی شکل دینے کے متعلق احکامات جاری کرتے رہے اور مسلسل اس پراجیکٹ کی مختلف تجویزات پر حکمانہ کاروائی ہوتی رہی ہے۔</p>	<p>(ج) آیا یہ بھی درست ہے کہ سابقہ وزیر اعلیٰ خیبر پختونخواہ نے اس اہم منصوبے کی فریڈیلٹی اور پی سی ون کی حتمی شکل دینے کے احکامات جاری کیے تھے؟</p>
<p>۱۔ منصوبے کی فریڈیلٹی رپورٹ WAPDA کے پاس موجود ہے۔ ۲۔ اس منصوبے سے ضلع ڈیرہ اسماعیل خان کی 1295000 ایکڑ اراضی سیراب ہوگی۔ ۳۔ یہ منصوبہ WAPDA بذریعہ کنسلٹنٹ تکمیل کرے گا اور اس کی ساری تجویزات WAPDA مہیا کرے گا۔ منصوبے کی چیدہ نکات سوال نمبر 31 کے ساتھ لف ہے</p>	<p>(د) اگر (الف)، (ب) و (ج) کے جوابات اثبات میں ہوں تو ۱۔ مذکورہ منصوبے کی فریڈیلٹی رپورٹ فراہم کی جائے۔ ۲۔ منصوبے سے جنوبی اضلاع کی کتنی زمین سیراب ہوگی؟ ۳۔ منصوبے کا ماسٹر پلان، پی سی ون اور مدت تکمیل کی تفصیلات بھی فراہم کی جائیں۔</p>

CHASHMA RIGHT BANK CANAL PROJECT (LIFT-CUM-GRAVITY)

Location

The proposed project is located on the Right Bank of Indus River in D.I.Khan District, KPK.

Salient Features

Feeder Canal

- Capacity 2,570 Cusecs
- Length 40.14 km

Pumping Station

- Capacity 2,557 Cusecs
- Lift 66.64 ft

Pumping Units

- Capacity 8 Units
- Type 6x353 cfs & 2x212 cfs
- Vertical mixed flow pump

Main Canal (Gravity Flow)

- Capacity 2,556 Cusecs
- Length 130.76km
- Command Area 295,774 Acres
- Total Water Requirement 1.187 MAF

Distributaries

- No. of Distributaries 28 Nos.
- Length 147.30 Miles
- Length of Minors 73.7 Miles

Execution by

Consultants

- M/s NESPAK (JV Lead Firm), M/s ACE, M/s SILT and M/s ECPAK for Review of Feasibility Study, Preparation of Detailed Engineering Design, Bidding Documents & PC-I
- Supervision Consultants being procured.

Funding Agency


65% by Federal Govt. and 35% by Khyber Pakhtunkhwa Govt.

PC-I Cost

Approved by- ECNEC on 07.10.2022 for Rs. 189,606.428 Million including FEC of Rs. 18,030.580 Million

Construction Period

5 years

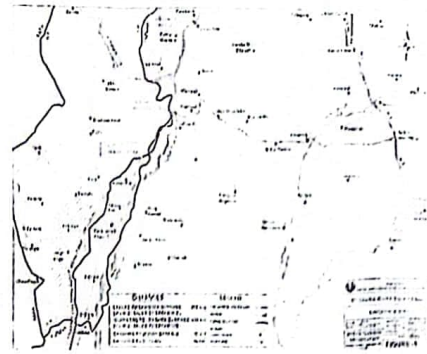

Sr. No.	Actions	Timelines	Responsible	Status
1	Detailed Engineering Design Consultants	01/07/2021 to 30/06/2023	WAPDA	All deliverables submitted viz: Detailed Engineering Design, BD, PC-I etc.
2	Procurement of Construction Supervision Consultants (CSC)	12/04/2023 to 31/03/2024	WAPDA	Technical evaluation finalized and financial proposal will be opened soon.
3	Initiating process of procurement of Contractors	12/04/2024 to 31/05/2025	WAPDA	Review of design and BD by CSC. PQ documents finalized, NIT for PQ yet to be published.
4	Mobilization of Contractors	12/2024	WAPDA	

Status:

- The Consultancy Agreement was awarded to M/s NESPAK (JV) on 28.06.2021 and the Consultants mobilized at site on 01.07.2021. The Consultancy Agreement has been extended upto 30-06-2023.
- Consultants have submitted the Design Report, Project Planning Report, Environmental & Social Impact Assessment Report, PC-I Proforma, Feasibility Study of Solar Panels PV Power Plant and 07 No. Contract Package Bidding Documents which are currently being finalized in light of comments from various WAPDA formations.
- As per Prime Minister directives, Pre-Qualification documents for Contractors have also been prepared. Pre-qualification process will be initiated soon.
- WAPDA initiated process for procurement of Construction Supervision Consultants (CSC) and Request for Proposals (RFP's) were submitted on 12.07.2023. Technical evaluation report finalized by the evaluation committee on 23rd December 2023.
- Item note thereof has been prepared to solicit approval of WAPDA Authority for ranking and opening of the financial proposals.
- Process for conducting the public hearing on the EIA report of this project was held at D.I.Khan city on 03.04.2024.
